


ClaytonGO: Foundation Plan Summary

Order Number:	N/A	Home Width:	30 FT 0 IN	Roof Load:	20 PSF	Use this QR Code to access DAPIA approved tables referenced within this design. Hover your iPhone camera over the code. For Android and other devices, download a QR Code reader. Questions? Email sitecompletionq&a@claytonhomes.com
Model Number:	946-46ESS32684AH VISION	Home Length:	68 FT 0 IN	Soil Bearing Cap:	1500 PSF	
Home Building Facility:	946	Outrigger Length (O.R.):	40.25 IN	Min. I-Beam Size:	10 IN	
		Chassis Spacing:	99.5 IN	Calculated Eave/Overhang:	12 IN	

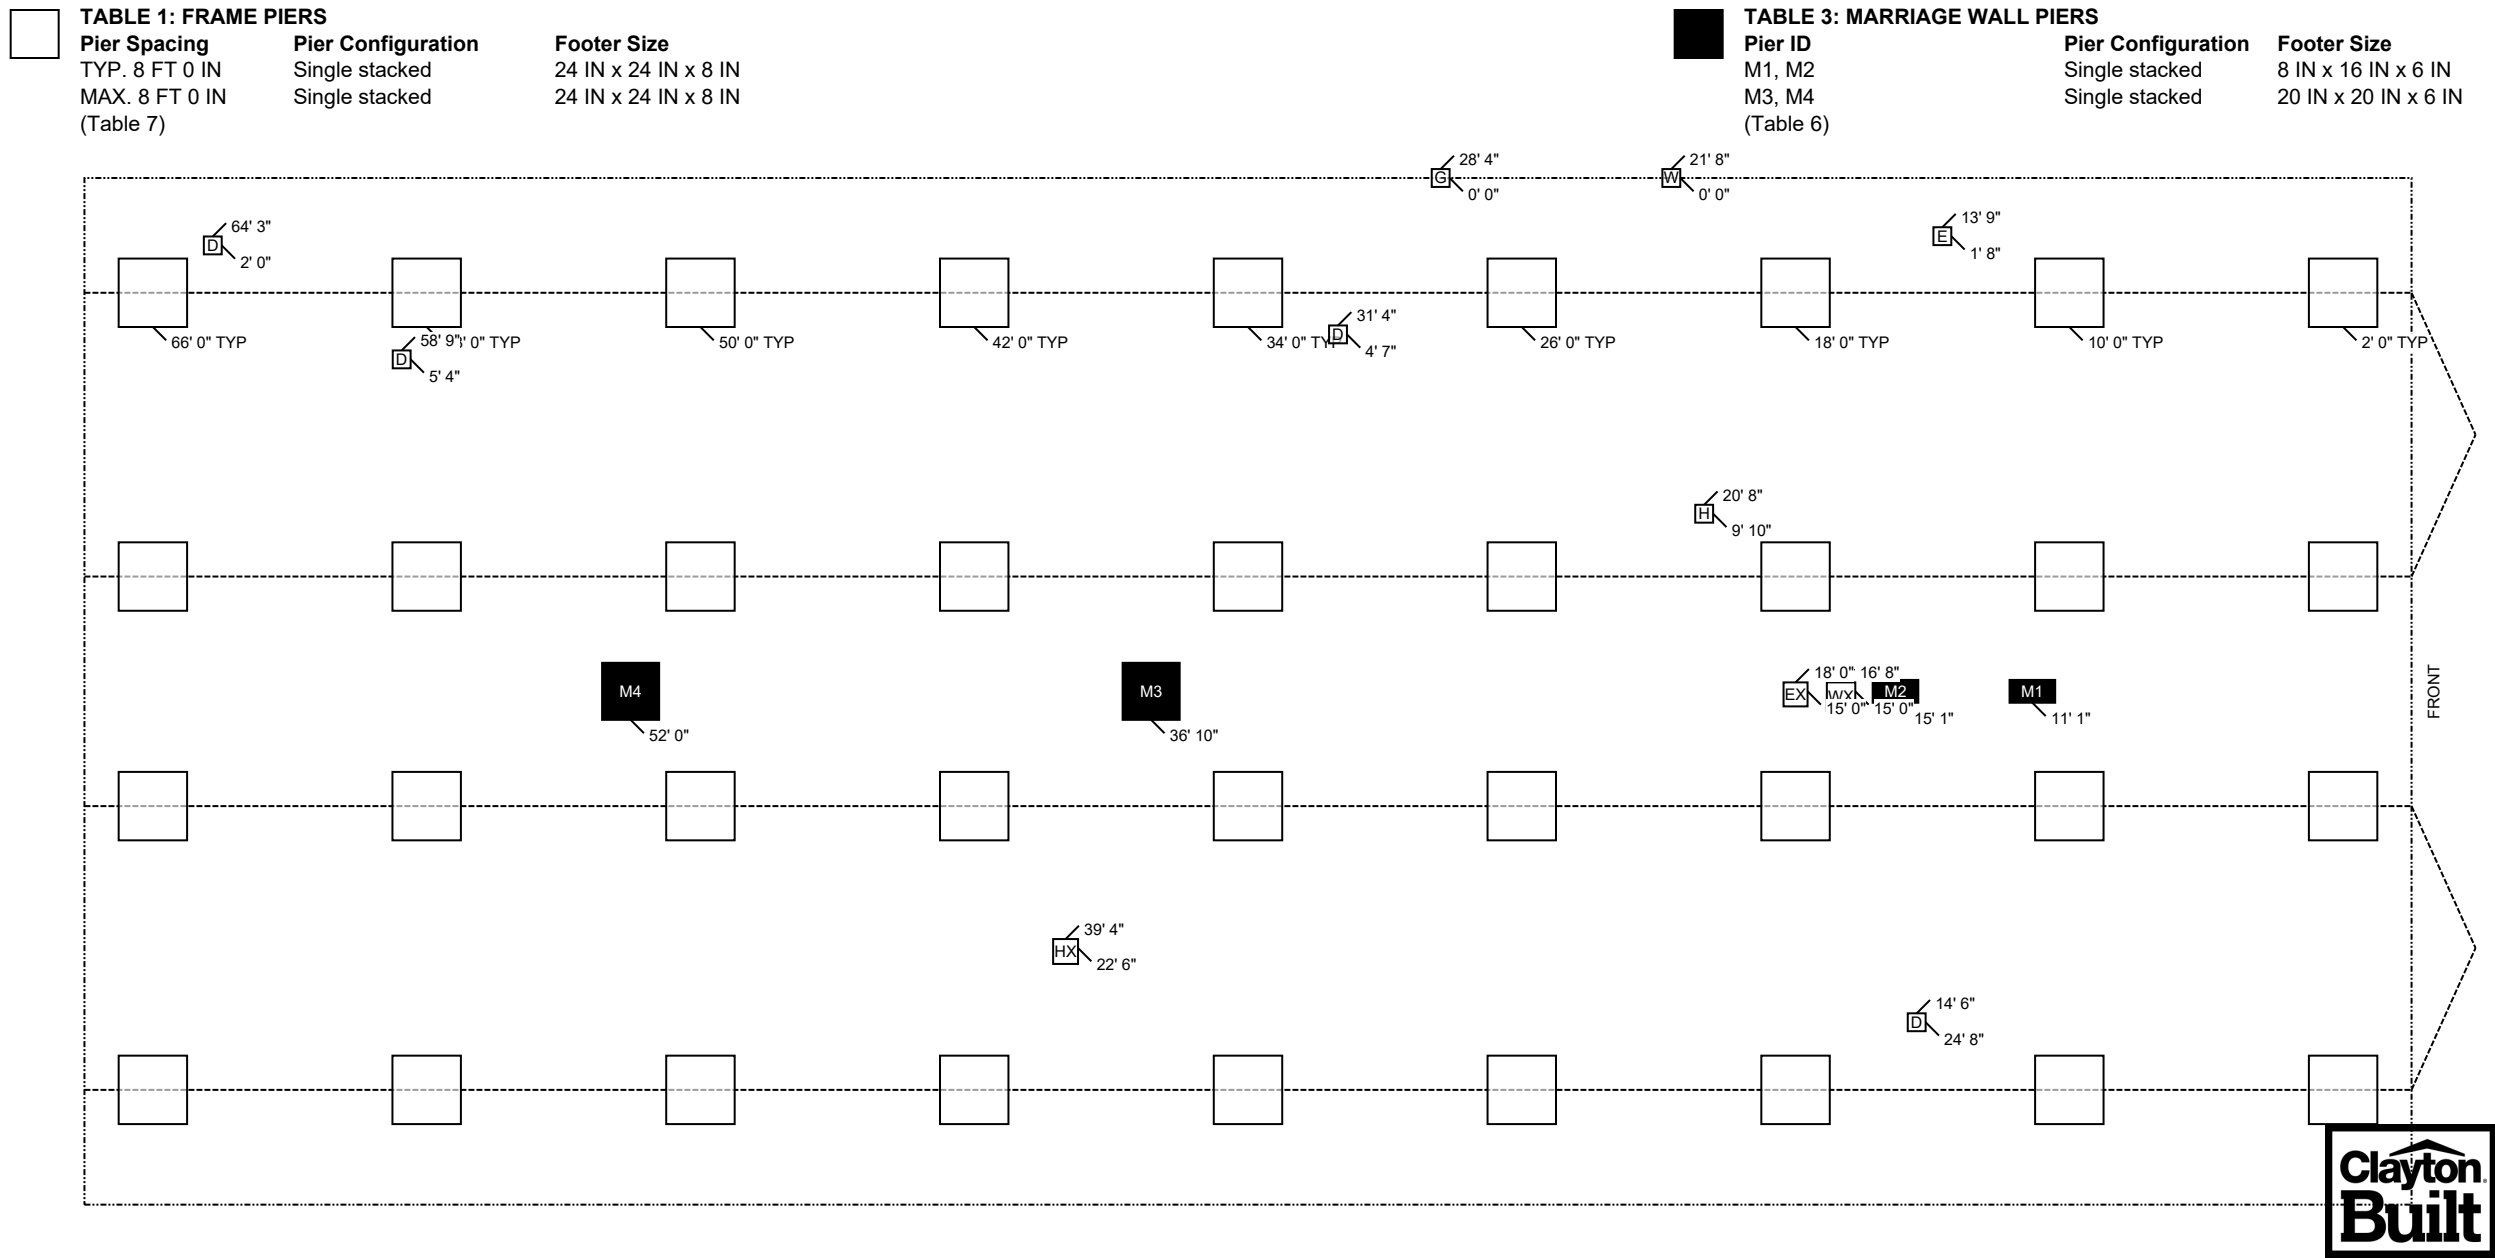

ClaytonGO: Foundation Plan Summary

Order Number:	N/A	Home Width:	30 FT 0 IN	Roof Load:	20 PSF	Use this QR Code to access DAPIA approved tables referenced within this design. Hover your iPhone camera over the code. For Android and other devices, download a QR Code reader. Questions? Email sitecompletionq&a@claytonhomes.com	
Model Number:	946-46ESS32684AH VISION	Home Length:	68 FT 0 IN	Soil Bearing Cap:	1500 PSF		
Home Building Facility:	946	Outrigger Length (O.R.):	40.25 IN	Min. I-Beam Size:	10 IN		
		Chassis Spacing:	99.5 IN	Calculated Eave/Overhang:	12 IN		

UTILITIES		LOCATION	
ID	UTILITY	LEFT	DOWN
D	Drain Drop	64 FT 3 IN	2 FT 0 IN
D	Drain Drop	31 FT 4 IN	4 FT 7 IN
D	Drain Drop	14 FT 6 IN	24 FT 8 IN
D	Drain Drop	58 FT 9 IN	5 FT 4 IN
E	Elec Entrance	13 FT 9 IN	1 FT 8 IN
EX	Elec Crossover	18 FT 0 IN	15 FT 0 IN
G	Gas Inlet	28 FT 4 IN	0 FT 0 IN
H	HVAC Drop	20 FT 8 IN	9 FT 10 IN
HX	HVAC Crossover	39 FT 4 IN	22 FT 6 IN
W	Water Inlet	21 FT 8 IN	0 FT 0 IN
WX	Water Crossover	16 FT 8 IN	15 FT 0 IN

- NOTES:**
- 1. FROST PROTECTION WILL BE PROVIDED BY PLACING FOOTERS BELOW FROST DEPTH OF 35 INCHES PER (FIGURE 5A) OR FROM LAHJ. Frost depth for interior footers may be taken as half with R5 skirting per (Table 5) [3285.312(b)]
 - 2. HOME HAS BEEN BUILT WITH ADDITIONAL FLOOR JOIST AT SIDEWALL OPENINGS TO ELIMINATE NEED OF SIDEWALL PIERS. SIDEWALL PIERS SHALL BE PLACED WHERE INDICATED BY PIER TAGS ON HOME.
 - 3. ALL FOOTERS WILL BE POURED CONCRETE. ALL SINGLE STACKED PIERS WILL HAVE A MINIMUM FOOTER THICKNESS OF 8 INCHES with footer depth extending below frost depth using 3,000 PSI minimum concrete (table 12)
 - 4. THIS PIER LAYOUT HAS BEEN DERIVED USING PE SEALED & DAPIA APPROVED INSTALLATION MANUAL AS OUTLINED ABOVE. PLEASE SEE INSTALLATION MANUAL FOR PE SEAL AND DAPIA APPROVAL. (Reference to Clayton Homes DAPIA approved Installation manual) [Reference to Federal Statutes 24 CFR Part 3280, 3285 or 3286]

